

## WORK COMPLETION REPORT

Contractor/Supplier	Unique Force General Contracting	P.O. No.	4500024946
Project/Capex Ref. No.		Supplier Quote No.	QTUF-20250600724
Project	Construction Of Caravans	Location	Al Ajbaan School, AL Shahama
Work Completed Date	07/10/2025	Report Date	08/10/2025
Job Type	<input checked="" type="checkbox"/> Electrical <input type="checkbox"/> Mechanical <input checked="" type="checkbox"/> Plumbing <input checked="" type="checkbox"/> Civil <input type="checkbox"/> Other _____		

Inspection Check Points:		Yes	No	Comments:
1.	Job has been executed as per the approved quotation	✓		
2.	The job has been completed in the time promised	✓		
3.	Quality of workmanship is satisfactory	✓		
4.	Materials used are as per the approved quotation	✓		
5.	The work area has been left clean & tidy	✓		

Sl. No.	DESCRIPTION OF SCOPE AS PER CONTRACT/ PO
1.	<p><b><u>General Site Work &amp; Foundations</u></b></p> <ul style="list-style-type: none"> <li>Demolition and removal of 2 existing caravans and their foundations.</li> <li>Construction of 2 new foundations with steps and block entrances.</li> <li>Rectification of the existing septic tank and all necessary drainage connections.</li> <li>External water and drainage connections for the toilet cabin, including trenching and backfilling.</li> <li>Supply and installation of new manholes (60x60 and 30x30).</li> <li>Application of primer, Fiber mesh, and final waterproofing coat for 2 units.</li> </ul>
2.	<p><b><u>Changing Room Caravan (12 x 3.6 M)</u></b></p> <ul style="list-style-type: none"> <li>Supply and installation of H-beam foundation, steel support frame, and 18mm cement board flooring.</li> <li>Walls constructed with 6mm cement board (exterior), 50mm Rockwool insulation, and 12mm fire-rated gypsum board (interior).</li> <li>60x60 gypsum ceiling, 1.55mm vinyl flooring, and wooden skirting installed.</li> <li>17 dugout plastic chairs with frames, 4 windows (90x90), and 3 aluminium doors installed.</li> <li>Client-provided AC units have been successfully installed.</li> <li>Complete roofing system with trusses and 0.5mm single-layer steel sheets installed.</li> <li>Exterior texture painting and interior smooth finish painting completed (Paint Colour as per client recommendation).</li> <li>All electrical works completed as per ADDC standards.</li> </ul>

## WORK COMPLETION REPORT

3.	<p><b><u>Toilet Caravan (6 x 3.6 M)</u></b></p> <ul style="list-style-type: none"> <li>• Supply and installation of H-beam foundation, steel support frame, and waterproofed 18mm cement board flooring.</li> <li>• Walls constructed with cement board and Rockwool insulation.</li> <li>• 60x60 aluminium ceiling and RAK floor and Wall tiles installed.</li> <li>• Installation of 5 round cut windows and 7 aluminium doors.</li> <li>• Complete roofing system (0.4mm sheets) and roof waterproofing installed.</li> <li>• Exterior texture painting completed (Paint Colour as per client recommendation).</li> <li>• All electrical and plumbing works, including RAK sanitary wares, exhaust fans, and lights, are complete.</li> </ul>
----	--

Photographs	
Before	
	
	
	

WORK COMPLETION REPORT

After	
Toilet Caravan (6 x 3.6 M)	
 <p>A photograph showing the foundation of the toilet caravan, which is a rectangular structure made of concrete blocks on a sandy ground. A red metal frame is visible in the background.</p>	 <p>A photograph showing the steel structure of the toilet caravan, which is a rectangular frame made of red metal beams. A yellow measuring tape is visible on the ground.</p>
 <p>A photograph showing the exterior of the toilet caravan with cement board installed. The structure is surrounded by a chain-link fence.</p>	 <p>A photograph showing the interior of the toilet caravan with cement board installed. A tripod stand is visible in the center.</p>
 <p>A photograph showing the exterior bulkhead structure of the toilet caravan, which is a rectangular structure made of metal and cement board.</p>	 <p>A photograph showing the interior of the toilet caravan with a toilet separation structure installed. The structure is made of metal and cement board.</p>
 <p>A photograph showing the interior of the toilet caravan with WC and drainer plumbing installed. The plumbing is made of metal and cement board.</p>	 <p>A photograph showing the interior of the toilet caravan with toilet plumbing installed. The plumbing is made of metal and cement board.</p>


## WORK COMPLETION REPORT



Toilet Exterior Joint Filling



Toilet Exterior Texture Painting



Installation of Toilet Ceiling Groove



Installation of Toilet 60 x 30 Wall & Floor Tiles



Installation Of Ceiling Tiles 60 x 60, Light and Smoke Detector



Installation of Window A/C, Basin & Basin Mixer



Installation of Window A/C, Basin & Basin Mixer



Installation of Basin & Basin Mixer



Installation of WC, Shattaf & Floor Trap



Installation of Toilet Door



WORK COMPLETION REPORT



Installation of Toilet Main Door



Installation of Toilet Entrance Steps With Non-Slippery Tiles



Installation of Switches for Toilet



Installation of Window Exhaust Fan



Toilet Manhole Foundation



Installation of Toilet Manhole Cover




Drainage













Cleaned Existing Septic Tank

WORK COMPLETION REPORT

	
Finished Toilet Caravan (6 x 3.6 M)	
Changing Room Caravan (12 x 3.6 M)	
	
Steel Structure and Foundation	Changing Room Caravan H-Beam Installation
	
Changing Room Caravan Steel Structure	Installation of Exterior Cement Board
	
Steel Structure for Changing Room Exterior Bulkhead	Exterior Bulkhead with Cement Board and Joint Filling
	
Installation of Roofing Sandwich Sheet	Waterproofing on the Roof

## WORK COMPLETION REPORT

 <p>Installation Of Ceiling Grooves</p>	 <p>Installation of 60 x 60 Ceiling Tiles, Ceiling Light, and Smoke Detector</p>
 <p>Installation of Window AC</p>	 <p>Installation of Window AC &amp; Application of Interior Smooth Painting</p>
 <p>Installation of DB</p>	 <p>DB</p>
 <p>Window Interior</p>	 <p>Window Exterior</p>
 <p>Separation Of Changing Rooms</p>	 <p>Changing Rooms</p>



## WORK COMPLETION REPORT




Self-Levelled Interior Floor




Vinyl Flooring and Benches



Switches (Schneider)

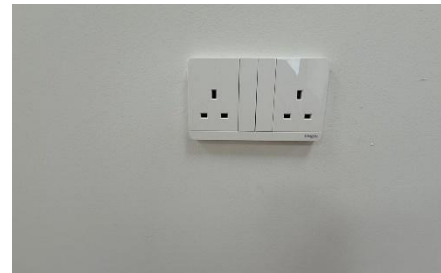

2 Gang Socket 6 Nos(Schneider)

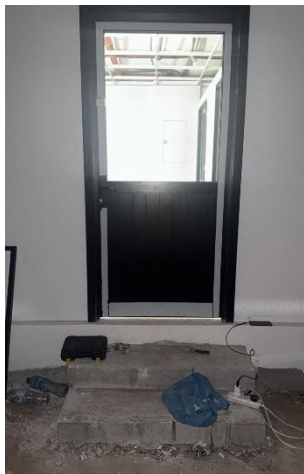

Changing Room Main Door Before



Changing Room Main Door



Changing Room Entrance Steps with Non-Slippery Tiles



Changing Room Caravan (12 X 3.6 M)



WORK COMPLETION REPORT



Changing Room Caravan and Toilet Caravan

Contractor Representative Name & Signature		Client Representative Name & Signature	
Muhammad Ali			

*[Handwritten Signature]*
